City of Huntington Beach - Cameron Lane NAV - WEEK AT A GLANCE - 8/21/20



General site view



The existing house is scheduled to be demolished Monday



Site view. SCE truck out on 8/20 to de-energize house and remove meter



Drone shot

OC Public Works | A&E Project Management
Integrity, Accountability, Service, Trust

Prepared by Totum

CITY OF HUNTINGTON BEACH
DEPARTMENT OF PUBLIC WORKS

integrated design construction management sustainability
totum

City of Huntington Beach - Cameron Lane NAV - WEEK AT A GLANCE - 8/28/20



Existing house demolished



Asphalt demolition in preparation for sewer lines by City



Installation of temp perimeter fencing



Ongoing water spraying to contain dust during degrubbing of project site


City of Huntington Beach - Cameron Lane NAV - WEEK AT A GLANCE - 9/4/20




Looking towards Cameron Lane.... And somone peeking in....



Cameron Lane view.

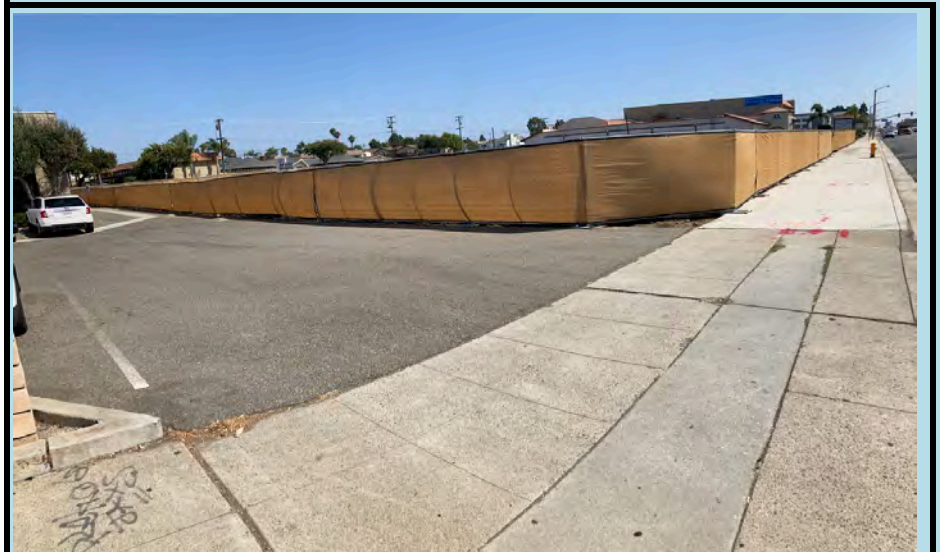

Corner of Beach and the commercial property.

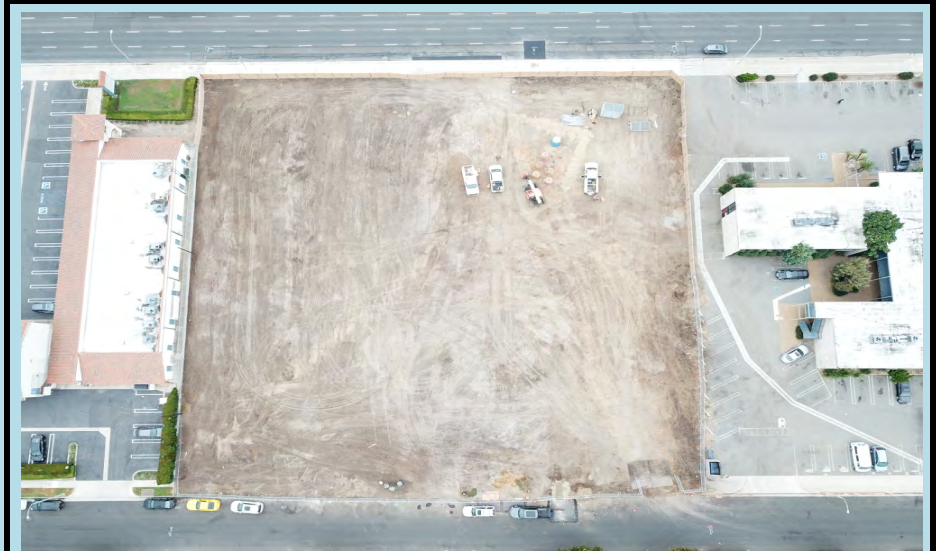

Drone shot. Site is cleared.

CITY OF HUNTINGTON BEACH
DEPARTMENT OF PUBLIC WORKS


integrated design construction management sustainability totum

Prepared by Totum

PublicWorks | A&E Project Management

MACRO-Z-TECHNOLOGY

City of Huntington Beach - Cameron Lane NAV - WEEK AT A GLANCE - 9/18/20

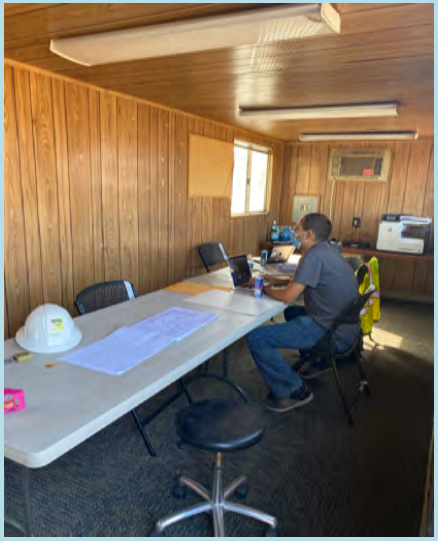



Off site (in road) City / Totum trailer set up and ready. Power coming next week



Site surveyed and staked. SWPPP's start next week along with grading



Mandatory sign posted. Totum have added some COVID poster on a temp basis. Larger to follow



City banner posted on side of trailer. Shall we add Sean's cell # ? lol

CITY OF HUNTINGTON BEACH
DEPARTMENT OF PUBLIC WORKS

Prepared by Totum

integrated design construction management sustainability totum

City of Huntington Beach - Cameron Lane NAV - WEEK AT A GLANCE - 9/25/20



Rumble strips delivered and installed



Grading and dust mitigation throughout job site



Northern area for Sprung Up location being compacted



Gravel delivery as base in preperation for asphalt installation

CITY OF HUNTINGTON BEACH
DEPARTMENT OF PUBLIC WORKS

Prepared by Totum

integrated design construction management sustainability
totum

City of Huntington Beach - Cameron Lane NAV - WEEK AT A GLANCE - 9/26/20



Watering of site during grading to keep dust levels down



Major milestone - 2" AC paving over base installed on north side, so sprung structure install can start on Monday.



Compaction of gravel base at north site



Gravel delivery as base in preparation for asphalt installation

CITY OF HUNTINGTON BEACH
DEPARTMENT OF PUBLIC WORKS

Prepared by Totum

integrated design construction management sustainability totum

City of Huntington Beach - Cameron Lane NAV - WEEK AT A GLANCE - 10/03/20



Temporary power pole being installed



Partial asphalt installation of Fire Lane



Sprung framing being erected



Aerial shot showing asphalt and Sprung with canvas

CITY OF HUNTINGTON BEACH
DEPARTMENT OF PUBLIC WORKS

Prepared by Totum

integrated design construction management sustainability totum


City of Huntington Beach - Cameron Lane NAV - WEEK AT A GLANCE - 10/09/20




Swaddles re-installed / repaired around perimeter



Drone view of progress

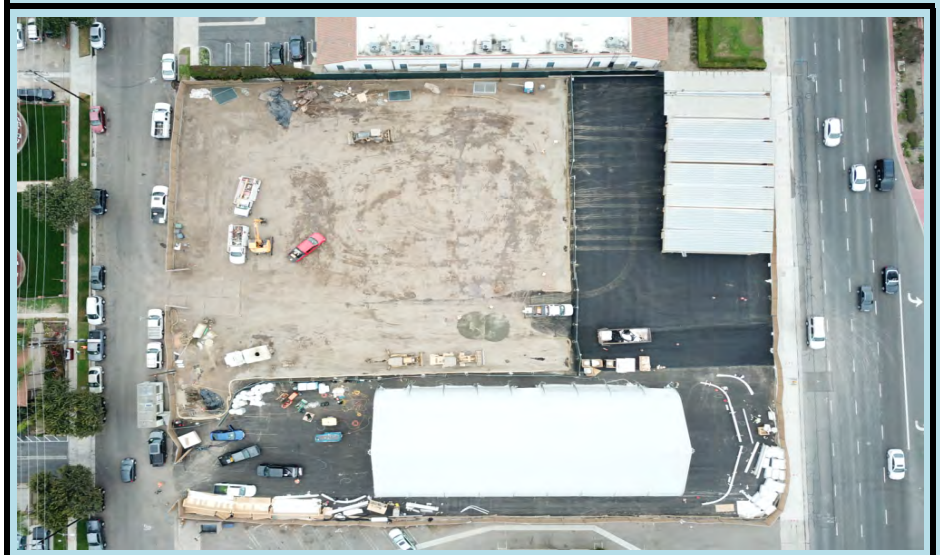

TTS mobilized, trenching and grading underway

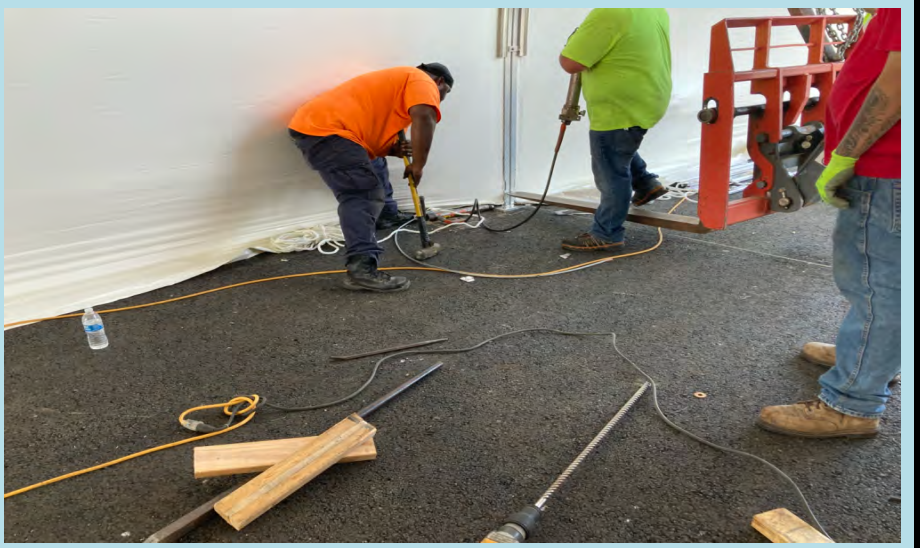

Frames being shifted over to make the structure taut.

CITY OF HUNTINGTON BEACH
DEPARTMENT OF PUBLIC WORKS


Prepared by Totum

integrated design construction management sustainability totum

City of Huntington Beach - Cameron Lane NAV - WEEK AT A GLANCE - 10/16/20



Utility trenching, with the plastic membrane installation, backfill, backfill and and utility piping underway.

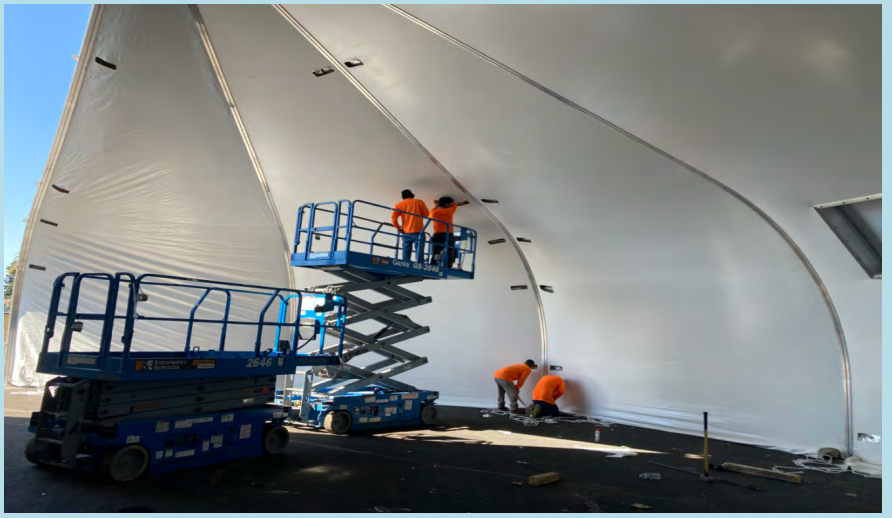

Sprung structure is now fully expanded and end pieces are being installed. The internal wall and partition walls should start within next couple of weeks.



Interior framing underway in trailers for Mercy House.



Drone shot of the status of the sprung structure.

CITY OF HUNTINGTON BEACH
DEPARTMENT OF PUBLIC WORKS

Prepared by Totum

integrated
design
construction
management
sustainability
totum

City of Huntington Beach - Cameron Lane NAV - WEEK AT A GLANCE - 10/24/20



Sprung partition wall installation



Drone photo of current site progress



Progress in Administration Offices trailer









Excavated dirt stockpiled, exported on trucks, continuous street sweeping, and ongoing site grading.

CITY OF HUNTINGTON BEACH
DEPARTMENT OF PUBLIC WORKS

Prepared by Totum

integrated design construction management sustainability totum

City of Huntington Beach - Cameron Lane NAV - WEEK AT A GLANCE - 10/31/20



Drone shot from Saturday. Trailers are almost placed in their final locations; asphalt almost complete.






Wrapping up asphalt; Inside of sprung structure. Electrical and HVAC underway.







Mercy admin, dining and laundry trailers in motion and set up.

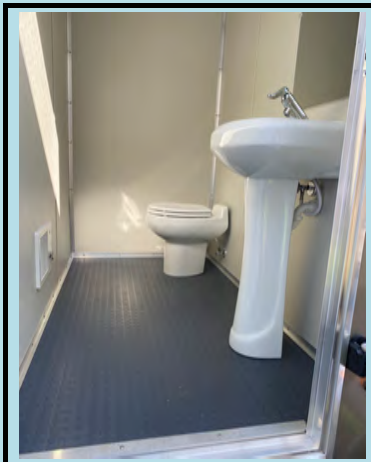





Restroom trailer from county is now on site. Hook up today.

CITY OF HUNTINGTON BEACH
DEPARTMENT OF PUBLIC WORKS

Prepared by Totum

integrated design construction management sustainability
totum

City of Huntington Beach - Cameron Lane NAV - WEEK AT A GLANCE - 11/6/20



Interior partitions underway in sprung structure



Flooring underway in the Mercy House trailers



Drone shot of the trailers placed and painting underway



Utility work ongoing

CITY OF HUNTINGTON BEACH
DEPARTMENT OF PUBLIC WORKS

Prepared by Totum

integrated design construction management sustainability totum

City of Huntington Beach - Cameron Lane NAV - WEEK AT A GLANCE - 11/13/20






CMU wall at Cameron underway; SCE worker connecting feeders for power; interior of dining hall; back ground - chainlink fence install underway



Interior of sprung structure; ongoing mechanical work, fire alarm and sprinkler work. Lighting is in.



Drone view




Installing CCTV cameras; concrete and track for sliding motorized gate

CITY OF HUNTINGTON BEACH
DEPARTMENT OF PUBLIC WORKS

Prepared by Totum

integrated design construction management sustainability totum

City of Huntington Beach - Cameron Lane NAV - WEEK AT A GLANCE - 11/21/20









Top L-R: Prepping floor for coating, blue 1st coat ; feeding the troops inc Mercy House; N side CMU @ Beach. 36".



Cameron 6' wall complete with cap; hoisting in the trash enclosure lid. Sidewalk substantially completed



NW corner prepared for new overflow trailer. Power stubbed as shown by the green conduit by light pole



Laundry room complete . Washers and dryers came today

CITY OF HUNTINGTON BEACH
DEPARTMENT OF PUBLIC WORKS

Prepared by Totum

integrated design construction management sustainability totum

City of Huntington Beach - Cameron Lane NAV - WEEK AT A GLANCE - 11/25/20



County restroom trailer relocated to SE corner of site to become Mercy staff restroom. Utilities were run to this location.



Interior of sprung flooring asphalt coating with contrasting exit path of travel





Painting of the overflow trailer; drinking fountains active.



Inside of overflow trailer. Finishes next week (flooring, paint, lighting etc)

CITY OF HUNTINGTON BEACH
DEPARTMENT OF PUBLIC WORKS

Prepared by Totum

integrated design construction management sustainability totum

City of Huntington Beach - Cameron Lane NAV - WEEK AT A GLANCE - 12/4/20



View from Cameron. Project goes live on Monday.



View of project from Beach. Project goes live on Monday. Everything is operational.



Huntington Beach opens huge tent for the homeless

The navigation center will offer a way for people to get on their feet. And it means the city can enforce anti in town.

Construction Manager Alejandro Pinel walks through the new Navigation Center on Tuesday, December 1, 2020. Bed frames – not yet spaced out – fill the shelter's men's area. The 11,600-square-foot "tension fabric" tent in Huntington Beach can house 174 homeless people with an additional overflow area. It also has 16 restrooms and 12 showers. The temporary structure was installed in just two months and will start housing people on Monday. (Photo by Mindy Schauer, Orange County Register/SCNG)

Press article. Albeit some errors







South wall complete. View of outdoor dining area and staff toilets; interior of sprung ready for occupancy.

CITY OF HUNTINGTON BEACH
DEPARTMENT OF PUBLIC WORKS

Prepared by Totum

integrated design construction management sustainability totum
